

REPORT TO: WEST OF ENGLAND COMBINED AUTHORITY COMMITTEE

DATE: 27 MARCH 2026

REPORT TITLE: TRANSPORT

RESPONSIBLE OFFICER: EXECUTIVE DIRECTOR OF TRANSPORT

<u>Key Decision</u>	Yes
----------------------------	------------

<u>Purpose of Report</u>

To provide an update to the West of England Mayoral Combined Authority (MCA) Committee and to secure approval from Committee on an appropriate delegated authority, ensuring decisions are reached in a timely manner.
--

<u>Recommendation</u>

That Committee:

- | |
|--|
| <ol style="list-style-type: none">1) Delegates authority to the West of England Combined Authority's Executive Director of Transport, in consultation with the equivalent unitary authority Directors, to issue a tender, award a contract, and establish contract and operational management arrangements for the next Integrated Micromobility Service contract. In the event of a consensus not being reached at Director level, decision making will be escalated to the West of England Combined Authority's Chief Executive Officer (CEO) in consultation with the unitary authority CEOs, as detailed in paragraph 1 – 23.2) Notes the submission of the detailed draft Local Transport Delivery Plan.3) Notes the outcome of the CRSTS re-baseline exercise.4) Delegates authority, to the West of England Combined Authority's Executive Director for Transport in consultation with the West of England Combined Authority S73 Officer, equivalent Directors from the Unitary Authorities, and S151 Officers from the Unitary Authorities for the approval of all remaining CRSTS change requests. In the event of a consensus not being reached at |
|--|

Director level, decision making will be escalated to the Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs, as detailed in paragraphs 58 - 87. In the event of a consensus not being reached at Chief Executive Officer level, decision making will be escalated to the Committee.

- 5) Delegates authority to the West of England Combined Authority's Executive Director for Transport in consultation with the West of England Combined Authority S73 Officer, equivalent Directors from the Unitary Authorities, and S151 Officers from the Unitary Authorities, for the approval of all remaining CRSTS business cases. In the event of a consensus not being reached at Director level, decision making will be escalated to the Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs as detailed in paragraphs 58 - 87. In the event of a consensus not being reached at Chief Executive Officer level, decision making will be escalated to the Committee.

Reasons for recommendations

The recommendations set out in the report will enable the delivery of key transport and infrastructure projects and priorities that have been previously agreed by the West of England MCA Committee. Over the next decade, the West of England MCA will deliver major projects that will transform our transport network for the benefit of residents in the region. Approval of the recommendations set out in this report will enable the MCA to progress its ambition to deliver a well-connected, accessible transport network that helps people get around quickly, safely, and sustainably in ways that support our region's environmental priorities.

Voting arrangements

In order to be carried, a decision on this matter requires a majority of the members present and voting, such majority is to include the Mayor. Each member present may cast one vote. If a vote is tied the decision is not carried. There is no casting vote. Co-opted members are not entitled to vote.


Publication Requirements

For publication.

Micromobility

Background

1. In July 2020, the Department for Transport (DfT) launched a national rental e-scooter trial. The trial period has subsequently been extended five times by the DfT, with the current national trial extended to May 2028.
2. Rental micromobility services were introduced in the West of England in October 2020 as part of the region's Future Transport Zone (FTZ) programme. The MCA procured a concession contract for e-scooter rental services.
3. In January 2023, the MCA re-tendered the micromobility concession contract with e-bike and e-cargo bike rental services added to the scope. This re-tendered service was defined as the Integrated Micromobility Service (IMS). The MCA holds the contract with the operator, and the MCA is responsible for the overall management of the contract. The contract commenced on 7th July 2023.
4. The Unitary Authorities (UA) work collaboratively with the MCA and operator to support the operational management of the service within their own authority area and to support the sharing of best practice with other UA colleagues.
5. The number of daily trips now regularly exceeds 10,000. Highlights shown below from the user survey undertaken by the MCA in summer 2025 demonstrate the key role the micromobility service now plays in the regional transport system.

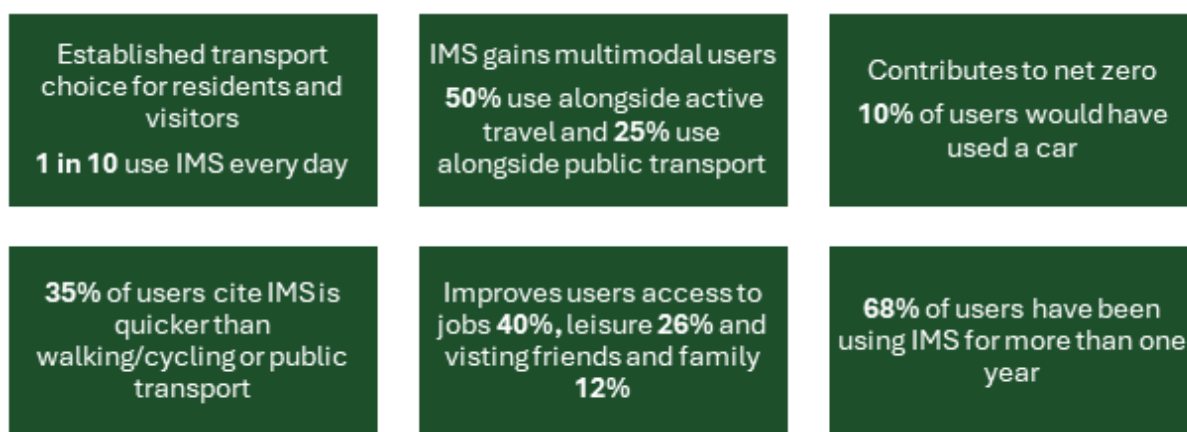

Key Considerations

6. The current IMS supplier contract expires on 6th July 2027 and cannot be extended beyond the current 4-year contract duration. A new contract needs to

be procured to ensure continuity of the IMS in the region.

7. The new IMS Contract will be a concession contract procured under the Procurement Act 2023.
8. The procurement documentation, including the contract specification and draft commercial terms, are being drafted in parallel with the recommendations going forward to MCA Committee. Engagement with Unitary Authority Directors on key aspects of the tender is planned prior to the tender being released.
9. The IMS contract will include provisions that require the MCA to approve in advance any changes to service parameters or operational requirements. This may include, among other things: price increases, changes to discounts, advertising permissions, approval of a penalty strategy, amendments to KPI thresholds. These operational contract decisions are not explicitly covered within the MCAs contract standing orders. A delegation is therefore requested to the Executive Director of Transport to put operational contract decision-making arrangements in place.

Alternative Options Considered

10. Not procuring a new IMS contract has been discounted because IMS is a key part of the region's transport system.

Consultation and Engagement

11. The IMS contract scope has been developed in close consultation between the MCA and UA officers, and with feedback from Avon & Somerset Police and Avon Fire & Rescue Service.
12. Feedback from users and non-users is regularly reviewed and will inform the development of the specification of the IMS contract.

Key Risks

13. Limited market interest leading to a lack of competition in the procurement process and reduced outcomes for the MCA.
 - The West of England is an attractive market for on-street micromobility rental companies due to the high existing usage of e-bikes and e-scooters. The risk can therefore be sufficiently mitigated by developing a specification and contract that responds positively to market feedback (where possible) and that is in line with the best practice found across other UK and European markets.

- The project team has undertaken regular market engagement and research during the existing contract. Pre-market engagement will be formally undertaken to inform the contract specification and other procurement documentation.

Diversity, Equity and Inclusion Implications

14. In progressing the proposed delegations relating to the micromobility tender, the Combined Authority will continue to have due regard to its duties under the Equality Act 2010 and the Public Sector Equality Duty. While this paper seeks approval for governance and decision-making arrangements rather than the contract specification itself, equality considerations will be embedded within the subsequent development of the service model, procurement documentation and contract management framework. This will include consideration of equitable geographic access, affordability, safety, digital accessibility and engagement with underrepresented communities, to ensure that the benefits of micromobility contribute to inclusive growth and improved access to sustainable transport across the region.

Climate Change Implications

15. Bristol City Council, Bath and North East Somerset Council, South Gloucestershire Council and the Mayoral Combined Authority have all signed climate emergency declarations. Following its declaration, the West of England Climate and Ecological Strategy and Action Plan (CESAP) set out the environmental priorities for the region. These priorities are reflected in the West of England's Growth Strategy, with the region aspiring to be nature positive and have climate resilient and decarbonised transport infrastructure.
16. The IMS project is contributing to the improvement of public transport, which will help to reduce car dependency and the associated greenhouse gas emissions, air pollution and congestion. The project reports that carbon saving from users switching from car/taxi/bus trips to e-scooters and e-bikes outweighs the carbon increase from those switching from walking/cycling trips to e-scooter. The trial to date has contributed to reduced carbon emissions across the region.

Financial Implications

17. There are no financial implications to the changing of the delegation regarding procuring a new IMS contract. Once the procurement is underway, it is expected that this will need to be led by the IMS project manager and this work will be funded through current concession fees and the MCA share of any IMS revenue

share income. The new concession fees should ensure that once in place, running the contract is cost neutral.

Legal Implications

18. Legal Services officers will work with IMS Service officers and Commercial officers to support the procurement exercise for the new IMS contract. This will include the selection and appointment of external legal advisers.

Human Resources Implications

19. There are no direct HR implications arising from this report. For situations where there is a need for more staff resource than currently exists, HR will work with the relevant officer/lead to ensure the request to recruit approvals and CLT approvals are in place, followed by the Combined Authority's recruitment or agency process to appoint all posts – including fixed term, permanent, interim, agency or contractor. Whilst not anticipated, in situations where funding is reduced, the Combined Authority's internal managing change and redeployment processes will be applied where applicable

Commercial and Procurement

20. Pre-market engagement, and research regarding the IMS market and financial/delivery models used are in progress. The findings of this will be used to develop and inform the Procurement Strategy, tender documentation and approach to market. The commercial team will develop the procurement strategy based on the use of competitive flexible procedure and ensure that the MCA can achieve best value for money.
21. As this is classified as a high priority gold contract (as prescribed by the MCA's contract segmentation tool), it is vital that the contract mechanisms allow for any poor performance to be managed effectively and concession fee or equivalent is bid at a realistic and achievable level.
22. It is anticipated that the commercial contract management activity will be managed by the centralised Commercial Contract Management team.
23. Commercial will ensure appropriate resources are allocated to support and deliver the procurement project. Commercial Board will be cited and approve the final procurement strategy and contract award report once the tender process has been completed.

Appendices

- None

Background papers

- None

West of England Mayoral Combined Authority Contact:

Report Author: *Oliver Coltman*

Contact Details: *Oliver.coltman@westofengland-ca.gov.uk*

Transport for City Regions (TCR) funding

Background

24. For the West of England Combined Authority area, the Transport for City Regions (TCR) funding allocation is a total grant of £752m for the period 2027/28 to 2031/32, made up of £693m capital funding and £59m revenue funding. Revenue funding has been allocated alongside TCR capital settlements to support the development of investment pipelines, and to build longer-term local transport planning and delivery capacity.
25. Since the confirmation of TCR funding in June 2025 the MCA has published its Growth Strategy, which sets a clear direction for growth in our region including North Somerset. The delivery of this important strategy is now a real focus and funding sources, such as TCR, will need to be prioritised to ensure that growth is realised. In addition, the West of England Transport Vision has been published, which focuses on developing a transport network that:
- can be trusted
 - is affordable, efficient to use
 - offers more journey choice
 - is ready for the future
 - can enable our region to thrive
26. TCR and CRSTS funding now form part of a wider Local Transport Consolidated Fund and DfT has commissioned Mayoral Strategic Authorities to produce a Local Transport Delivery Plan (LTDP), setting out details of how all the available funding has been prioritised, with details of schemes and interventions or programmes and packages of spend. The MCA is required to submit a detailed draft of the LTDP with all spending for 2026/27 and an outline plan to 2029/30 (2031/32 for TCR), by 20 March 2026 and a final LTDP to 2029/30 (2031/32 for TCR) should be submitted to DfT by 18 September 2026. DfT has also set out its expectation that the LTDP is updated and published annually.

Key Considerations

27. As reported to the [October 2025 Committee](#), this funding will be utilised to start delivering against the Growth Strategy and continue delivering the region's adopted Joint Local Transport Plan.
28. The October 2025 Committee gave approval to committing £140.78m from the TCR programme to fund the expanded CRSTS programme. This will

provide early delivery of projects within the TCR funding period. With other commitments to revenue and maintenance there is £392.22m of TCR funding remaining to commit.

29. As part of the programme development a number of place-based workshops were held with unitary authority partners in December 2025. The purpose of these workshops was to identify the transport interventions that were required to enable growth in each of the growth zones. As part of this process a total of 91 scheme proposals were identified. Of those schemes there are cost estimates for 52 schemes, which range from £888m - £1.7 bn.
30. In addition to the workshops with the UA partners input has also been sought from the West of England Bus Operators Association because of the link to the update to the Enhanced Partnership and the need to join up the planning of capital and revenue investment.

Draft Local Transport Delivery Plan

31. As noted in paragraph 26 the first DfT deadline to submit a draft LTDP was on 20 March 2026. Using the delegations approved by Committee in October 2025 the table below summarises the LTDP submission:

<i>Funding area</i>	<i>£m</i>
Integrated Transport Block / Maintenance	185
Revenue	59
Completion of CRSTS programme	141
Bus	150
Rail	150
Mass Transit focusing on areas as outlined in the mass transit section of the Transport Vision: • The West Innovation Arc: for instance we are looking at increasing rail frequency between the WIA and Bristol Temple Quarter as well as orbital routes • The Bristol to Bath Growth Zone (A4 corridor) • The North Somerset Growth Gateway, including the airport • Improved public transport connections to the Somer Valley Growth Zone	150
Active Travel	50
Unlocking development sites	20
Transport Innovation	20
Mayoral Local Priority fund	15

TOTAL	940
TCR settlement	752
overprogramming	188

32. The TCR programme will focus investment on transport improvements that address strategic constraints and support growth, developing interventions aligned to adopted and emerging spatial and economic strategies.
33. It is important to note that this is a draft plan and the development of the final LTDP will be an iterative process, informed by work that will be undertaken between now and September 2026.

2026/27 scheme development programme

34. In addition to the revenue funding that is available throughout the TCR period there is also £9.5m of capability funding that can be used to develop the project pipeline. This work is critical to position our region well for significantly increased funding settlements in future spending reviews and as the MCA moves towards an integrated settlement.
35. One of the key learnings from the CRSTS programme is the time required for business case development. It is therefore important that delivery of the TCR programme does not go from a standing start from April 2027 and that work on business case development is able to start ahead of this in preparation for delivery during the TCR funding period.
36. It is proposed that the revenue funding is utilised to progress the emerging strategic priorities, including an allocation for bus reform for considering what model of bus operation is suitable for our region. The October 2025 committee approved delegated authority to the West of England Mayoral Combined Authority's Executive Director of Transport, in consultation with the equivalent Unitary Authority Directors, to allocate CRSTS capacity and capability funding and TCR revenue funding. The following development programme has been approved.

Development projects	2026/27	2027/28
	(£)	(£)
Future Bus Network Development	500,000	
Bus Reform studies	1,000,000	1,000,000
Henbury Line frequency improvements (to feasibility design)	750,000	1,500,000

Brabazon to Bristol Parkway link (to SOBC)	200,000	500,000
New stations development, e.g. Saltford, Ashton Gate and / or alternative South Bristol location (to SOBC)	600,000	1,500,000
Battery Electric Train Infrastructure (to OBC)	650,000	650,000
Station accessibility (to feasibility design)	250,000	1,000,000
Mass transit - scope validation focusing on areas as outlined in the mass transit section of the Transport Vision: • The West Innovation Arc: for instance we are looking at increasing rail frequency between the WIA and Bristol Temple Quarter as well as orbital routes • The Bristol to Bath Growth Zone (A4 corridor) • The North Somerset Growth Gateway, including the airport • Improved public transport connections to the Somer Valley Growth Zone • Linking locations across Bristol city centre, including enabling seamless onward journeys from Bristol Temple Meads	5,000,000	7,000,000
Active Travel scheme development	150,000	1,850,000
Active travel behaviour change	650,000	150,000
Transport Innovation – scope development	250,000	
Place-based business cases / Growth Zone Transport studies	150,000	
Current existing commitments	11,500,000	8,050,000
Total revenue spend	21,650,000	23,200,000
RDEL Funding Net position (CRSTS)	16,000,000	
RDEL funding (TCR from DfT profile)	2,766,000	11,341,000
Capacity fund	9,510,000	
Total revenue income	28,276,000	11,341,000

37. Some of the development funding will be utilised to complete specific pieces of work to inform the development of the Final LTDP. For example, a study to identify where investment is required to deliver improved bus journey times and reliability and, separately, an analysis of the strategic gaps in the region's active travel network.

Next steps

38. Ahead of the submission of the final LTDP in September 2026 further scheme prioritisation will take place to refine the detail of the programme. Modelling, benefits mapping and assurance activities will be carried out to ensure the programme is able to effectively deliver its key outcomes. Early business case development work will also commence in 2026/27 so that we are not commencing the programme from a standing start in April 2027.

Alternative Options Considered

39. As outlined in the October 2025 committee report alternative options would be to allocate TCR funding either based on population or through a bidding process. Neither of these approaches are considered appropriate as they do not take a regional, strategic approach or represent the optimal use of funding.
40. There could be a wide range of alternative options in relation to how the remaining £392m of TCR funding is allocated against the modes and / or other funding priorities. The programme as outlined above are considered to represent the right balance between funding priorities based on meeting the MCA's strategic objectives, the information available at this time and identifying work required to be able to meet the September deadline for the final LTDP.

Consultation and Engagement

41. As noted in paragraph 29 and 30, a number of place-based workshops with our unitary authority partners have been held and engagement has also happened with the West of England Bus Operators Association to inform the development of the programme.
42. Discussions have been held with the TCR Steering Group, which includes representatives from the unitary authorities, and with Executive Directors for Transport. TCR was also subject to discussion at the Transport Advisory Board meeting held on 6 March 2026.

43. The development of the final LTDP, ready for submission to DfT in September 2026, will be a collaborative process between the MCA and the Unitary Authorities. As part of this collaboration there will be more frequent engagement and consultation at both a political and officer level, including more discussions with the Transport Advisory Board and dedicated workshops with Executive Directors and unitary authority Transport Leads.
44. Schemes included in the programme will be subject to public engagement and consultation as appropriate.

Key Risks

45. The October 2025 committee report identified the ability to identify a suitable level of local contributions as a risk. Whilst this remains a risk it is now at a lower level as a result of DfT confirming that a local contribution target of 5% will be applied to consolidated capital funding, excluding the final year of CRSTS funding.
46. The other risk identified, failing to reach consensus on the programme that will best deliver against the regional strategic objectives, remains but will be mitigated through the development work identified to inform the final LTDP and continued engagement with officers and Members from the unitary authorities.

Diversity, Equity and Inclusion Implications

47. The recommendations within this report have been considered in line with the Equality Act 2010 and the Public Sector Equality Duty. Transport investment can affect communities differently, particularly in relation to disability, age, sex and socio-economic status. An inclusive-by-design approach will therefore be embedded through delivery, ensuring that accessibility, safety, affordability and equitable geographic distribution of benefits are considered as core principles. Proportionate engagement and ongoing monitoring will support the identification and mitigation of any unintended adverse impacts, aligning delivery with the Combined Authority's commitment to inclusive growth and improving quality of life for all residents across the West of England.

Climate Change Implications

48. Bristol City Council, Bath and North East Somerset Council, South Gloucestershire Council and the Mayoral Combined Authority have all signed climate emergency declarations. Following its declaration, the West of England Climate and Ecological Strategy and Action Plan (CESAP) set out the environmental priorities for the region. These priorities are reflected in the West

of England's Growth Strategy, with the region aspiring to be nature positive and have climate resilient and decarbonised transport infrastructure.

49. Any modal shift from individual, combustion engine car use through electric bus and active travel will see operational reductions in carbon emissions. Construction of the supporting infrastructure also needs to factor in emission reductions, to ensure the net impact is still an emission reduction. This means a strong focus on adopting best practice in materials use and site management, as well as taking a strategic view on decarbonisation of the network.
50. As the LTDP is developed in detail and moves to delivery, environmental considerations should be integrated as early as possible. This includes ensuring all infrastructure is resilient to both current and future climate impacts (based on expected longevity of the project) and that all opportunities are taken to reduce impacts on natural systems, and where feasible, enhancements made. Within the overall funding envelope, a small but sufficient resource should be allocated to ensure climate impacts are managed and nature positive decisions are fully integrated.

Financial Implications

51. The TCR programme proposes a total expenditure of £939.78m, which is 25% higher than the available budget of £752m. Given the historic trend of project delivery taking longer than initially anticipated, this level of over-programming is considered prudent to help maximise the use of available funding within the TCR timeframe. As a result, it is expected that not all proposed projects will reach completion within the £752m budget envelope.
52. The recommendation also seeks approval to allocate £10.5m of revenue funding to a range of early development projects in 2026/27. Sufficient funding is available to support this, with the MCA due to receive £9.51m in CRSTS and £2.766m in TCR revenue funding during 2026/27. In addition, there is a forecast £16m headroom carried forward from 2025/26. CRSTS and TCR programme support activity is expected to utilise £11.5m of this funding, with any remaining balance carried forward to support TCR development activity in 2027/28.
53. There is currently a TCR revenue funding deficit forecast in 27/28 of £5m, meaning that not all of the development work set out can take place within these two years. It is possible that the Mass Transit Programme will enter into the OBC stage earlier and would therefore not need the full £12m revenue funding suggested in the table above, as it would move to capital expenditure. Another option that could be explored would be delaying some development expenditure

into future years so that the work schedule is more in line with the £11.34m we will be receiving each financial year for TCR capacity funding.

Legal Implications

54. In October 2025 the West of England Combined Authority Committee made the following delegation:

Approved delegated authority to the West of England Combined Authority's Executive Director of Transport, in consultation with the equivalent Unitary Authority Directors, the approval and submission of the Transport for City Regions (TCR) plan to the Department for Transport as set out in paragraphs 1-56. In the event of a consensus not being reached at Director level, decision making to be escalated to the West of England Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs.

55. This report provides an update to Committee on the draft TCR plan.

Human Resources Implications

56. There are no direct HR implications arising from this report. For situations where there is a need for more staff resource than currently exists, HR will work with the relevant officer/lead to ensure the request to recruit approvals and CLT approvals are in place, followed by the Combined Authority's recruitment or agency process to appoint all posts – including fixed term, permanent, interim, agency or contractor. Whilst not anticipated, in situations where funding is reduced, the Combined Authority's internal managing change and redeployment processes will be applied where applicable.

Commercial and Procurement

57. Early stage proposal development is underway to determine appropriate future procurement models to support delivery of the TCR programme. Proposals are focused on improving engagement with key partners, increasing resilience across the supply chain, increasing diversity of suppliers engaged across the programme and driving value through commercial and competitive processes where possible. This may include the development of a TCR specific framework or arrangement to enable re-engagement with the market. All major procurement exercises will likely fall under the PA23 regulations with specific tender processes followed accordingly.

Appendices

None

Background papers

None

West of England Mayoral Combined Authority Contact:

Report Author: Louise McBride

Contact Details: louise.mcbride@westofengland-ca.gov.uk

CRSTS

Background

58. In January 2026, the City Region Sustainable Transport Settlements (CRSTS) programme provided an update to the Committee on the CRSTS re-baseline exercise. At that time the programme was still working through the re-baseline exercise and took an action to update the Committee with the outcome. The programme has now completed the re-baseline exercise and DfT are reviewing the proposal in their DfT Change Board before the end of the financial year. The purpose of this paper is to update Committee on the outcome of the re-baseline.

59. To note as per the October Committee the re-baseline exercise included:

- approved an allocation of £140.78m Transport for City Regions (TCR) funding to complete the CRSTS programme based on WebTAG standard guidance for optimism bias.
- noted the requirement to contractually commit by March 2027.
- noted the revised programme end date of March 2029.
- agreed a delegation to the Executive Director of Transport, in consultation with the equivalent Directors of the UAs, to submit a change request to the DfT with a re-baselined programme, and
- set out a revised set of guiding principles for managing the programme.

60. The MCA Committee decision in October 2025 resulted in the new funding allocations in the table below which are proposed to be the final allocations for the four organisations to manage the remaining delivery of CRSTS. Each organisation has an increased allocation.

Table 1 – Overall funding allocations for the programme

Org	Pre-Oct 25 Allocations (£m)	Revised Allocation as per Oct 25 (£m)	Proposed Allocations as per CRSTS Board approval (£m)
MCA	147.31	171.81	168.87*
BCC	161.87	179.31	179.31
B&NES	62.55	69.99	69.99
SGC	162.36	163.52	163.52
TOTAL BUDGET	534.09	584.63	581.69
CRSTS funding	443.85	443.85	440.91*
TCR funding as per Oct 25 Committee	0.00	140.78	140.78

TOTAL FUNDING	443.85	584.63	581.69
----------------------	---------------	---------------	---------------

*Change in local match funding contribution for Bath to Bristol Strategy Corridor (BBSC) allocation in BANES area.

Key Considerations

61. Overall, aside from changes to spend profiles and milestones, the re-baseline change request includes changes to scope and budget allocations but it remains in line with the October 2025 Committee funding position. £140.78m is still required from TCR funding.
62. The programme still has a degree of uncertainty on its scope, profile, and funding requirements. Thirty-one out of fifty-seven projects do not yet have an approved full business case (FBC) or in contract for construction. Further individual changes at a project level, and updates to the programme's schedule are therefore expected as schemes continue to mature. A list of these schemes and the status of their scope is included in this report.
63. A summary of the changes to projects' timescales are shown in Appendix 1.
64. Following a discussion with the CRSTS Board the programme is seeking to ensure it clarifies its delegations and streamline its approach to the approvals process.
65. **Business case approvals** – the [July 2024 Committee](#) approved the clarification that the July 2022 Committee decision, which granted a delegation to the Director of Infrastructure of the Mayoral Combined Authority in consultation with the UA Directors of Infrastructure for business case approvals for those projects within the CRSTS programme, applied to all projects in the CRSTS programme and approved an increase in the value to £8m and below.
66. The September 2024 delegated the authority to approve change requests, funding applications and business cases for the CRSTS1 programme to the Chief Executive of the West of England Mayoral Combined Authority in consultation with Unitary Authority Chief Executives. In the absence of consensus between the Chief Executives such matters will revert to the Committee. All delegated decisions made will be reported to the next Committee.
67. The January 2025 Joint Committee delegated the approval of the EDF reallocations and delegated the approval of funding applications, business cases or change requests for schemes in the City Regions Sustainable Transport Settlement (CRSTS) programme drawing on the EDF, to the Chief Executive of

the West of England Mayoral Combined Authority in consultation with Unitary Authority Chief Executives.

68. The Committee is requested to consolidate both delegations into one delegation:

- Committee is requested to delegate the approval of all remaining business cases to the Executive Director for Transport in consultation with the West of England Combined Authority S73 Officer, equivalent Directors from the Unitary Authorities, and S151 Officers from the Unitary Authorities. In the event of a consensus not being reached at Director level, decision making will be escalated to the Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs. In the event of a consensus not being reached at Chief Executive Officer level, decision making will be escalated to the Committee.

69. **Change request approvals** – the [September 2024 Committee](#) delegated authority to approve change requests, funding applications and business cases for the CRSTS1 programme to the Chief Executive of the West of England Mayoral Combined Authority in consultation with Unitary Authority Chief Executives. In the absence of consensus between the Chief Executives such matters will revert to the Committee. All delegated decisions made will be reported to the next Committee.

70. The January 2025 Joint Committee delegated the approval of the EDF reallocations and delegated the approval of funding applications, business cases or change requests for schemes in the City Regions Sustainable Transport Settlement (CRSTS) programme drawing on the EDF, to the Chief Executive of the West of England Mayoral Combined Authority in consultation with Unitary Authority Chief Executives.

71. The Committee is requested to consolidate both change request delegations into one delegation:

- Committee is requested to delegate the approval of all remaining change requests to the Executive Director for Transport in consultation with the West of England Combined Authority S73 Officer, equivalent Directors from the Unitary Authorities, and S151 Officers from the Unitary Authorities. In the event of a consensus not being reached at Director level, decision making will be escalated to the Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs. In the event of a consensus not being reached at Chief Executive Officer level, decision making will be escalated to the Committee.

72. **Early works fund approvals** – the [January 2026 Committee](#) approved an amendment to the CRSTS delegation on Early Works Funding (EWF) applications to enable the Executive Director for Transport in consultation with the West of England Combined Authority S73 Officer, equivalent Directors from the Unitary Authorities, and S151 Officers from the Unitary Authorities to approve Early Works Funding applications.
73. **Maintenance Challenge Fund** – the July 2022 Committee delegated the responsibility for the maintenance challenge fund (£32m) and non-highway maintenance fund (£1m) to the Director of Infrastructure of the Combined Authority in consultation with the UAs Directors of Infrastructure. In the absence of unanimous agreement, the delegation reverts to the Combined Authority Chief Executive in consultation with the Unitary Authority CEO's. There will be regular reporting on CRSTS as a standing item at the CEO's meetings.

Alternative Options Considered

74. The alternative options considered included not submitting a rebaseline change request to the Department for Transport. However, this has been discounted because DfT have formally asked the MCA for an updated position following the change in DfT's guidance in 2025. Therefore, a zero response is not acceptable. DfT have been informed of the timescales and were aware that the programme had previously planned to present a re-baseline report to Committee in October 2025 followed by detailed change requests from each authority. The grant conditions for the programme require a change request, due to the change in the grant conditions and the considerable number of changes in the milestones and funding profile.
75. The alternative option considered for the recommendation to consolidate the delegations is that the existing delegations remain. This has been discounted given:
- the CRSTS re-baseline exercise is complete with each authority having an envelope of funding and revised milestone dates and project allocations to work within.
 - The improvements in governance that have been implemented in 2025 with the CRSTS Board.
 - The majority of projects have now had funding awarded and the majority of projects are in delivery, meaning there are fewer business cases remaining to be considered.

Consultation and Engagement

76. This report has been endorsed by the CRSTS Board which includes the Executive Director of Transport and S73 officer from West of England Combined Authority, and Directors and S151 officers from Bristol City Council, South Gloucestershire Council and Bath and North East Somerset Council.

Key Risks

77. **Contractually committed milestone** – there is a risk that some schemes may not be contractually committed by March 2027. The re-baseline change request significantly reduces this risk with revised milestones confirmed by each authority. However, approximately £72m of the programme's allocation has contractually committed dates close to the March 2027. In addition, some concerns have been raised about the proximity of elections and the ability to commit to construction projects when an administration might change. Officers are reviewing options.
78. **Cumulative impact of construction** – as the programme delivery is back-ended a programme wide risk has been identified regarding the cumulative impact of construction on the transport network, communities and local economy in city centres. The extension of the programme for an additional two years has provided opportunities to re-phase schemes. In addition to this a review of the programme has been carried out – including a cumulative impact assessment with modelling. The results of which currently show that the impact is potentially less severe than previously assumed, this is due to some re-phasing, increased maturity of plans and improved data sharing. However, the data currently includes a high degree of assumptions and unknowns. Therefore, this risk remains a high rated risk for the programme. Ongoing transparency, monitoring and collaboration between the Combined Authority, Highways Authorities, transport operators and operations teams is essential.
79. **Impact on bus operations** – there is a risk that due to the location construction works, there will be significant re-routing of buses required, affecting the efficiency and effectiveness of bus operations. The programme is working closely with highways authorities and bus operators to manage impacts and consider bus routes and bus stop locations. In addition to this the UAs and MCA teams run a monthly session with bus operators to understand and support the impacts of construction. Positive feedback on these meetings has been received to date.

80. **Risk to benefits** - Scope reductions may reduce benefits relative to cost, making Value for Money (VfM) harder to demonstrate at FBC. Benefits and costs will need to be assessed at FBC stage to ensure compliance with DfT requirements.

Diversity, Equity and Inclusion Implications

81. The recommendations within this report have been considered in line with the Equality Act 2010 and the Public Sector Equality Duty. Transport interventions can affect communities differently, particularly in relation to disability, age, sex and socio-economic status. An inclusive-by-design approach will be embedded through subsequent stages of development and delivery, ensuring that accessibility, affordability, safety and equitable geographic distribution of benefits are considered as core principles. Proportionate engagement and ongoing monitoring will support the identification and mitigation of any unintended adverse impacts, aligning the proposals with the Combined Authority's commitment to inclusive growth and improving quality of life for all residents across the West of England.

Climate Change Implications

82. The MCA has committed to tackling the climate and nature emergencies, and confirmed this with further statements in the regional growth strategy. Enabling the delivery of transport interventions that provide alternative choices to using internal combustion engine private cars can help to reduce their associated environmental impacts. Projects should also ensure they are preparing for the unavoidable impacts of climate change, ensuring resilience is built into every stage. Projects that change scope should check that the benefits are still being delivered.

Financial Implications

83. Any overspend within a delivery partner's allocation will need to be dealt with by cost efficiencies or scope adjustments of that programme; all the DfT funding has been allocated and there is no contingency held in the central programme. The programme still carries significant financial risks – immaturity of cost estimates £295m pre-FBC, ability to forecast accurately, requirement to contractually commit by March 27. Projects which have contractually committed milestones close to March 27 have a value of £75.2m. Mitigation: Ongoing monitoring is required on milestones, moving to cost of work done – project to be set up to maintain focus and drive this work at more speed.

Legal Implications

84. On 17 October 2025 the MCA Committee delegated authority to the West of England Combined Authority's Executive Director of Transport, in consultation with the equivalent Unitary Authority Directors, the approval of the final re-baselined CRSTS delivery Plan and the submission of a programme level change request to the Department for Transport as set out in paragraphs 1-56 of the Report to Committee. In the event of a consensus not being reached at Director level, decision making to be escalated to the West of England Mayoral Combined Authority's Chief Executive Officer (CEO) in consultation with the Unitary Authority CEOs.

Human Resources Implications

85. There are no direct HR implications arising from this report. For situations where there is a need for more staff resource than currently exists, HR will work with the relevant officer/lead to ensure the request to recruit approvals and CLT approvals are in place, followed by the Combined Authority's recruitment or agency process to appoint all posts – including fixed term, permanent, interim, agency or contractor. Whilst not anticipated, in situations where funding is reduced, the Combined Authority's internal managing change and redeployment processes will be applied where applicable

Commercial and Procurement

86. Focus on improving key processes, particularly cost estimating, (to support budgeting) cost forecasting (to improve in-flight cost control on cost reimbursable contracts) and Cost to Complete (to improve focus on deliverability) will be central to ensuring financial outcomes are realised and potential implications recognised earlier in the contracting process. A number of improvements to processes, including robust adherence to forecasting requirements and clearly defined thresholds for approvals are in development and will further support programme delivery.
87. All procurement requirements identified for the remainder of the term will be evaluated for compliance with PA23, if required by threshold limits. Existing framework arrangements will typically be leveraged for the remaining term to minimise duplication or contractual complexity and maximise engagement with the existing supply chain.

Appendices

- Appendix 1 – CRSTS schemes, allocations, milestones for each authority

West of England Mayoral Combined Authority Contact:

Report Author: *Nuala Waters*

Contact Details: *Nuala.Waters@westofengland-ca.gov.uk*

Appendix 1 – CRSTS schemes, allocations, milestones following the CRSTS rebaseline

MCA Delivery Plan

88. The Committee approved a budget allocation of £171.81m. Adjustments since then reduce the MCA envelope slightly to £168.87m, reflecting changes in local contributions.
89. The information providing the details of the MCA delivery plan changes can be found in Tables 2 - 6.
90. The re-baseline request covers scope and benefits changes for Bath to Bristol Strategic Corridor, budget allocations, funding profiles, milestones. There is a potential for further changes as the programme completes consultations for the remaining sections.
91. A summary of major funding allocation changes include:
- Micromobility reduction (-£1m)
 - Scope is scalable; therefore, funding has been reduced to accommodate funding requirements elsewhere in the programme.
 - Tap on Tap Off phase 2 – (£-0.16m)
 - reduction in risk budget
 - MetroWest Phase 2 (+£24.93m)
 - As per October Committee the project is increasing its allocation from £10m to £34.93m
 - BBSC BANES (-£2.813m) *
 - Reduction in B&NES match to 20% of total DfT funding has reduced the local contribution budget, therefore the overall budget was £47m it is now £44.187m
92. Changes to FBC and construction dates to consider changes to consultation and design timelines are shown in the tables below. The MCA re-baseline request remains aligned with the October 2025 Committee funding position. While milestone delays are significant in BBSC projects, the overall programme is deliverable within the revised budget envelope. MetroWest Phase 2 uplift is a critical enabler for regional rail improvements, and governance safeguards are in place for projects requiring further scope clarification.

93. Table 2 MCA allocations

Project	Previous Baseline (£m)	Revised Baseline (£m)	Variance (£m)
BBSC Bristol Short Term	37.9	37.9	0
BBSC Bristol Long Term	4.0	4.0	0
BBSC BANES	47.0	44.187	-2.813*
M32	10.80	10.80	0
Tap on Tap off	2.08	1.92	0.16
Lawrence Hill	6.77	6.77	0
Metro West Phase 1	27.22	27.22	0
Metro West Phase 2	10.00	34.93	+24.93
Micromobility Parking	2.00	1.00	-1.00
Cycle Hangars	0.16	0.16	0
TOTAL	147.93	168.87	+20.94

Table 3 MCA previous Milestones

Project	FBC	Contractually Committed	Construction Start	Construction Complete
BBSC Bristol Short Term	Jan 26	N/A	Dec 25	Mar 27
BBSC BANES	Jan 26	N/A	Oct 25	Mar 27
BBSC Bristol Long Term	Mar 27	N/A	N/A	n/a
M32	Mar 27	N/A	N/A	n/a
Tap on Tap off	Jan 22	N/A	Feb 22	Mar 27
Lawrence Hill	Oct 25	N/A	May 26	Mar 27
Metro West Phase 1	July 25	N/A	Sept 25	Mar 28
Metro West Phase 2	Oct 25	N/A	North Filton – July 25	North Filton – Mar 26
Micromobility Parking	N/A – not yet approved			

Table 4 - Milestones Revised

Project	FBC	Contractually Committed	Construction Start	Construction Complete
BBSC Bristol Short Term	Route 1 (3-8) July-26 Routes 2 & 9 Mar-29	Route 1 (3-8) – Sept-26	Route 1 (3-8) Sept-26	Route 1 (3-8) Mar-29

BBSC BANES	Section 4-6 – July-26	Section 4-6 – July-26 Section 3 – July-26	Section 4-6 Sept-26 Section 3 - June-27	Section 4-6 Sept-26 Section 3 – Mar-29
BBSC Bristol Long Term	OBC – Mar-27 FBC – Oct-28	N/A	N/A	N/A
M32	March-27	N/A	N/A	N/A
Tap on Tap off	Jan-22	Feb-22	Feb-22	Mar-27
Lawrence Hill	Oct-25	Oct-25	May-26	Mar-27
Metro West Phase 1	Aug-25	Sept-25	Sept-25	Mar-28
Metro West Phase 2	Oct-25	North Filton – July-25	North Filton – July-25	North Filton – Mar-26
Micromobility Parking	Mar-26	Nov-26	Nov-26	Mar-27

Table 5 – Milestones variance

Project	FBC	Contractually Committed	Construction Start	Construction Complete
BBSC Bristol Short Term	+7 months	N/A	+9 months	+25 months
BBSC BANES	+6 months	N/A	+11 months	+25 months
BBSC Bristol Long Term	+19 months	N/A	N/A	N/A
M32	0	N/A	N/A	N/A
Tap on Tap off	0	N/A	0	0
Lawrence Hill	0	N/A	0	0
Metro West Phase 1	+1 month	N/A	0	0
Metro West Phase 2	0	N/A	0	0
Micromobility Parking	N/A	N/A	N/A	N/A

Table 6 – current baseline scope documents and indication of potential or actual changes

Project	Status	Changes
BBSC Bristol Short Term	Pre-FBC	Section 2 Routes 2&9 are deferred in the schedule (currently contractually committed by March 2027) and the rescoped to comprise development of an OBC and FBC only within the CRSTS funding deadline of March 2029.

		Section 1 Routes 1 and 2-8 have gone to public consultation and will be delivered as a stand-alone FBC. This is a change from the previous approach, in which a single FBC was to be delivered for all routes in BCC Phase 1.
BBSC BANES	Pre-FBC	Revised options for Section 3 (Keynsham Bypass) are under review. To avoid delaying Sections 4–6, Section 3 will be deferred in the programme and taken forward as a stand-alone FBC. It will still be contractually committed for delivery by March 2027 by being included as 'Deferred Scope' within the build contract, as set out in the BBSC Procurement Strategy. Options for Sections 4–6 was subject to public consultation from October to December 2025 and will be progressed through a standalone FBC. This represents a change from the previous approach, which proposed a single FBC for all sections within the B&NES area. Bath to Bristol Railway Path lighting removed. Extension to Brassmill Lane Bridge removed
BBSC Bristol Long Term	Pre-OBC	None
M32	Pre-OBC	None
Tap on Tap off	Delivery	None
Lawrence Hill	Delivery	None
Metro West Phase 1	Delivery	None
Metro West Phase 2	Delivery	None
Micromobility Parking	Feasibility	None

Bath & North East Somerset (B&NES) Delivery Plan

94. The revised B&NES delivery plan reflects scope reductions and reprofiling to enable projects to be contractually committed by March 2027 within the approved allocation of £69.99m. Adjustments have been made to keep the programme deliverable, cost effective, and aligned with grant conditions. Given the reductions in scope, an updated cost forecast is required on these projects to validate their current cost position. It is proposed to accept the position for now but validate the cost position on these schemes and report the outcome of this work to the board.

Table 7 - B&NES allocations

Project	Previous Baseline (£m)	Revised Baseline (£m)	Variance (£m)
Bath City Centre: Phase 1	5.65	6.816	1.166
Bath City Centre: Phase 2	2.07	1.171	-0.899
Bath City Centre: Phase 3	0.8	0.8	0
Somer Valley Links	17.97	22.7	4.73
Bath Liveable Neighbourhood	9.45	9.446	-0.004
Fielding's Bridge	0.04	0	-0.04
Bath Walking, Wheeling and Cycling Links	4.41	13.238	8.828
Midsomer Norton Walking and Cycling Links	1.44	2.58	1.14
Scholars Way	6.02	6.234	0.214
Somer Valley Enterprise Zone	10	2.33	-7.67
Bath Quays Bridge Pedestrian Cycle Links	4.7	4.675	-0.025
TOTAL	62.55	69.99	+7.44

Table 8 – B&NES previous Milestones

Project	FBC	Contractually Committed	Construction Start	Construction Complete
Bath City Centre: Phase 1	Dec-25	N/A	Mar-26	Mar-27
Bath City Centre: Phase 2	Dec-25	N/A	Apr-26	Nov 26
Bath City Centre: Phase 3	N/A	N/A	N/A	N/A
Somer Valley Links	Jan-26	N/A	Jan-26	Mar-27
Bath Liveable Neighbourhood	Sep-24	N/A	Sep-24	May-26
Fielding's Bridge	N/A	N/A	Descoped	Descoped
Bath Walking, Wheeling and Cycling Links	Oct-25	N/A	Jan-26	Aug-26
Midsomer Norton Walking and Cycling Links	Sep-25	N/A	Apr-24	Feb-27
Scholars Way	Jul-25	N/A	Jul-25	Oct-26
Somer Valley Enterprise Zone	Mar-25	N/A	Sep-25	Nov-26
Bath Quays Bridge Pedestrian Cycle Links	Oct-24	N/A	Sep-25	Jun-26

Table 9 – B&NES Milestones revised

Project	FBC	Contractually Committed	Construction Start	Construction Complete
Bath City Centre: Phase 1	Dec-25	Jan-26	Mar-26	Mar-27
Bath City Centre: Phase 2	Mar-26	Apr-26	Apr-26	Aug-26
Bath City Centre: Phase 3	N/A	N/A	N/A	N/A
Somer Valley Links *	Jan-26	Apr-26	Mar-26	Mar-27
Bath Liveable Neighbourhood	Sep-24	Jan-26	Oct-25	Dec-26
Fielding's Bridge	N/A	N/A	Descoped	Descoped
Bath Walking, Wheeling and Cycling Links*	Jun-26	May-26	Aug-26	Jan-27
Midsomer Norton Walking and Cycling Links	Jun-26	Sep-26	Jan-27	Jan-28
Scholars Way	Jul-25	Jul-25	Jul-25	Sep-26
Somer Valley Enterprise Zone	Nov-25	Nov-26	Feb-26	Mar-27
Bath Quays Bridge Pedestrian Cycle Links	Jul-25	Sep-25	Sep-25	Jun-26

*Further change request required on revised dates for phases

Table 10 – B&NES Milestones Variance Months

Project	FBC	Contractually Committed	Construction Start	Construction Complete
Bath City Centre: Phase 1	0	N/A	0	0
Bath City Centre: Phase 2	+3	N/A	0	-3 months
Bath City Centre: Phase 3	N/A	N/A	N/A	N/A
Somer Valley Links	0	N/A	+2 months	0
Bath Liveable Neighbourhood	0	N/A	+13 months	+7 months
Fielding's Bridge	N/A	N/A	Descoped	Descoped
Bath Walking, Wheeling and Cycling Links	+8 months	N/A	+7 months	+5 months
Midsomer Norton Walking and Cycling Links		N/A		
Scholars Way	0	N/A	0	-1 month
Somer Valley Enterprise Zone	+8 months	N/A	+5 months	+4 months
Bath Quays Bridge Pedestrian Cycle Links	+9 months	N/A	0	0

Table 11 - B&NES scope changes

Project	Status	Amendments
Bath City Centre: Phase 1	Delivery	No. FBC approved Jan 26
Bath City Centre: Phase 2	Pre-FBC	Remove mobility hubs, continue development VMS & checkpoint if still feasible within time/budget
Bath City Centre: Phase 3	Pre-OBC	No
Somer Valley Links	Pre-FBC	Split into phases. Phase 1 – Hub x4, 1A – Bear Flat, W&C x7, 2 – 5 W&C, Wellsway – continue development, & checkpoint if still feasible within time/budget
Bath Liveable Neighbourhood	Delivery	Remove London Rd, Pulteney Estate
Fielding's Bridge	Cancelled	None descoped
Bath Walking, Wheeling, and Cycling Links	Pre-FBC	Remove Oldfield School Route part 1, RUH Links North, continue development Oldfield school route part 2 & checkpoint if still feasible within time/budget, add K&A Canal Route
Midsomer Norton Walking and Cycling Links	Pre-FBC	Remove Cycling route
Scholars Way	Delivery	Remove Combe School
Somer Valley Enterprise Zone	Pre-FBC	Remove thicket mead, cycle path thicket mead to Wickes, CPO works, keep cycle lane
Bath Quays Bridge Pedestrian Cycle Links	Pre-FBC	Remove extension to or through Churchill Bridge Gyratory

South Gloucestershire Council (SGC) Delivery Plan

95. The changes brought forward by South Gloucestershire Council re-baseline change request are mostly adjusting delivery timelines and financial profiles for CRSTS projects. As the grant conditions are now extended to spend beyond March 2027, SGC are looking to adjust their profiles accordingly by updating construction timelines and including time for post construction activities (e.g., snagging, Road Safety Audit Stage 3). These changes ensure continued delivery within available resources but reflect a shift in how and when the allocated funding is used. £10.12m million is proposed to be reprofiled into 2027/2028. This includes a proportion of some projects' risk budgets to be reallocated across projects following a risk review. £2.3m of risk is to be released from A38 (£679,657) and Bradley Stoke Way (£1,620,343) to be reallocated to Charfield to cover increased costs from Network Rail contracts. An overview of new allocations is shown below:

Table 12 – SGC allocations

Project	Previous Baseline (£m)	Revised Baseline (£m)	Variance (£m)
Bradley Stoke Way Corridor	27.38	23.974	-3.406
Thornbury to North Bristol A38 Corridor	39.2	36.065	-3.135
Thornbury Corridor Programme Development	3.331	3.33	-0.001
Chipping Sodbury Corridor Programme Development	2.86	2.765	-0.095
A432 Sections 1-3	15.32	13.77	-1.55
A432 Badminton Road (4-8) corridor	15.6	15.4	-0.2
A432 Station Road (S9) corridor	0.05	7.201	7.151
Charfield Rail Station	39.5	41.78	2.28
Yate Spur Walking and Cycling	5.24	5.973	0.733
Alveston Hill Cycleway	5.93	6.07	0.14
Getting About in Yate	3	3.159	0.159
Getting About in Thornbury	3	3.129	0.129
Bristol to Bath Railway Path	1	0.904	-0.096
TOTAL	161.411	163.52	2.109

Table 13 - SGC previous Milestones

Project	FBC	Contractually Committed	Construction Start	Construction End
Bradley Stoke Corridor	Oct-24	N/A	Sep-24	Dec-26
Thornbury to North Bristol A38 Corridor	Oct-24	N/A	Sep-24	Mar-27
A432 Sections 1-3	Jul-25	N/A	Jan-25	Mar-27
A432 Badminton Road (4-8) Multimodal corridor	Mar-25	N/A	Jan-25	Mar-27
A432 Station Road (S9) Multimodal corridor	May-26	N/A	Jan-25	Mar-27
Charfield Rail Station	Jan-25	N/A	Mar-25	Mar-27
Yate Spur Walking and Cycling	Sep-24	N/A	Dec-24	Mar-27
Alveston Hill Cycleway	Nov-24	N/A	Feb-25	Dec-26
Getting About in Yate	Oct-25	N/A	Jan-26	Oct-26

Getting About in Thornbury	Jan-26	N/A	Oct-26	Feb-27
Bristol to Bath Railway Path	Jan-25	N/A	Jun-25	Mar-25

Table 14 - SGC Milestones revised.

Project	FBC	Contractually Committed	Construction Start	Construction End
Bradley Stoke Corridor	Oct-24	Jan-25	Feb-25	Jun-27
Thornbury to North Bristol A38 Corridor	Oct-24	Jan-25	Mar-25	Sep-27
A432 Sections 1-3	Jan-25	Jan-25	Jan-25	Mar-27
A432 Badminton Road (4-8) Multimodal corridor	Jan-25	Feb-25	Mar-25	Dec-27
A432 Station Road (S9) Multimodal corridor	Jan-25	Apr-26	May-26	Dec-27
Charfield Rail Station	Jul-25	Aug-25	Jan-25	Dec-27
Yate Spur Walking and Cycling	Sep-22	Mar-26	Apr-26	Sep-28
Alveston Hill Cycleway	Jan-25	Feb-25	Mar-25	May-27
Getting About in Yate	Jun-26	Oct-26	Oct-26	Mar-27
Getting About in Thornbury	Mar-26	Jul-26	Jul-26	Feb-27
Bristol to Bath Railway Path	Nov-25	Jan-26	Jan-26	Mar-27

Table 15 - SGC Milestones Variance

Project	FBC	Contractually Committed	Construction Start	Construction End
Bradley Stoke Corridor	0	N/A	+5 months	+6 months
Thornbury to North Bristol A38 Corridor	0	N/A	+6 months	+6 months
A432 Sections 1-3		N/A		
A432 Badminton Road (4-8) Multimodal corridor	-2 months	N/A	+2 months	+9 months
A432 Station Road (S9) Multimodal corridor	-16 months	N/A	+16 months	+9 months
Charfield Rail Station	+6 months	N/A	-2 months	+9 months
Yate Spur Walking and Cycling		N/A	+16 months	+18 months
Alveston Hill Cycleway	+2 months	N/A	+1 month	+5 months
Getting About in Yate	+8 months	N/A	+9 months	+5 months
Getting About in Thornbury	+2 months	N/A	-3 months	0

Bristol to Bath Railway Path	+10 months	N/A	+7 months	+24 months
------------------------------	------------	-----	-----------	------------

Overview of Bristol City Council's programme (BCC) changes

96. The BCC re-baselining change request includes some changes to project allocations to reflect the revised total allocation to Bristol City Council of £179.31m. Milestone changes reflect the revised programme end date. Changes to scope include the removal of A37-A4018 Park St from the CRSTS funded programme and some others within specific projects as set out in the tables below.

Table 16 - BCC allocations

Project	Previous Baseline (£m)	Revised Baseline (£m)	Variance (£m)
Bristol City Centre business case work	4.18	4.18	0.00
Temple Way	4.88	4.94	0.06
Union Street	5.64	19.38	13.74
Bond Street	0.00	4.74	4.74
Redcliffe Roundabout	0.00	6.03	6.03
Bedminster Bridges	14.15	13.61	-0.54
A4 Portway Corridor	14.34	23.10	8.76
Portway P&R Hub	2.34	2.14	-0.20
Stockwood Preparatory Business Case	2.99	2.81	-0.18
WP1 - Victoria Street / Colston Ave	5.57	5.57	0.00
WP2 - Southern Section	5.47	5.47	0.00
WP3 - Central Section	1.04	1.04	0.00
WP4 - Active Travel	0.00	1.71	1.71
WP5 - North View	0.00	0.40	0.40
A4018 (Passage Road)	6.44	6.63	0.19
Bristol Bridge	1.62	1.37	-0.25

Bedminster Green	10.51	9.90	-0.61
A38 South Metrobus Extension	4.03	3.49	-0.54
East Bristol Liveable Neighbourhood	5.94	5.94	0.00
Streetspace 1	1.39	1.39	0.00
Streetspace 2	1.52	1.52	0.00
South Bristol Liveable Neighbourhood	1.35	1.35	0.00
Harbour Walkway	9.81	9.81	0.00
Bristol Temple Quarter	12.10	12.10	0.00
Regional Cycle Centre	15.40	15.63	0.23
Cotham Hill	0.22	0.22	0.00
Concorde Way	0.40	0.45	0.05
Bristol unallocated general	0.00	14.39	14.39
Total	161.89	179.31	17.42

Table 17 - BCC Milestones current

Name	FBC Date	Contractually committed date	Construction Start Date	Construction Complete
Temple Way	Apr-25	N/A	Nov-25	Oct-26
Union Street	Apr-26	N/A	Jun-26	Sep-27
Bond Street	May-25	N/A	Feb-26	Mar-27
Redcliffe Roundabout	Jan-25	N/A	Aug-25	May-26
Bedminster Bridges	Sep-25	N/A	Sep-25	Mar-27
A4 Portway Corridor	Jan-25	N/A	Feb-25	Mar-27
Portway P&R Hub	Oct-23	N/A	Jan-25	Oct-25
WP1 - Victoria Street / Colston Ave	Feb-24	N/A	Oct-24	Jan-26
WP2 - Southern Section	Jan-25	N/A	Jul-25	Oct-26
WP3 - Central Section	May-25	N/A	Sep-25	Mar-27

WP4 - Active Travel	Oct-25	N/A	Feb-26	Mar-27
WP5 - North View	Jan-27	N/A	n/a	n/a
A4018 (Passage Road)	Jan-20	N/A	Dec-23	Nov-25
Bristol Bridge VMS	Completed	Completed	Completed	Completed
Bedminster Green	Completed	Completed	Completed	Dec-25
A38 South Metrobus Extension	Aug-25	N/A	Jan-26	Jul-26
East Bristol Liveable Neighbourhood	May-26	N/A	Oct-25	Nov-26
Streetspace 1	Nov-24	N/A	Dec-24	Sep-25
Streetspace 2	Jun-25	N/A	Sep-25	Mar-26
South Bristol Liveable Neighbourhood	Dec-25	N/A	Feb-26	Jul-26
Harbour Walkway	N/A	Completed	Nov 22	Oct-25
Bristol Temple Quarter	Aug-25	N/A	Apr-26	Apr-27
Regional Cycle Centre	Sep-25	N/A	Jan-26	Mar-27
Cotham Hill	Completed	Completed	Completed	Completed
Concorde Way	Aug-25	N/A	N/A	Mar-27

Table 18 - BCC Milestones revised.

Name	FBC Date	Contractually committed date	Construction Start Date	Construction Complete
Temple Way	Mar-25	Sep-25	Dec-25	Oct-26
Union Street	May-26	Jun-26	Aug-26	Nov-27
Bond Street	Jun-26	Nov-26	Apr-27	Aug-28
Redcliffe Roundabout	Feb-26	Jun-26	Jul-26	Aug-27
Bedminster Bridges	Mar-26	Jun-26	Jul-26	Aug-27
A4 Portway Corridor	Oct-24	Sep-25	Mar-26	May-27
Portway P&R Hub	Nov-23	Jan-25	Feb-25	Feb-26
WP1 - Victoria Street / Colston Ave	Mar-24	Sep-24	Jan-25	Jun-26

WP2 - Southern Section	Jan-25	Aug-25	Nov-25	Jul-26
WP3 - Central Section	Mar-25	n/a	n/a	n/a
WP4 - Active Travel	Aug-26	Jan-27	Mar-27	Jul-27
WP5 - North View	Jan-27	n/a	n/a	n/a
A4018 (Passage Road)	n/a	Sep-24	Jan-25	Mar-27
Bristol Bridge VMS Signals	Completed	Completed	Completed	Completed
Bedminster Green	Completed	Completed	Completed	Dec-25
A38 South Metrobus Extension	Aug-25	Sep-25	Jan-26	Sep-26
East Bristol Liveable Neighbourhood	Jun-26	Aug-26	Oct-26	Mar-27
Streetspace 1	Oct-24	Nov-24	Feb-25	Sep-25
Streetspace 2	Apr-26	Jun-26	Jul-26	Jun-27
South Bristol Liveable Neighbourhood	Aug-26	Jan-27	Mar-27	Jul-28
Harbour Walkway	Completed	Completed	Sep-25	Feb-26
Bristol Temple Quarter	Sep-25	Jan-26	Jul-26	Mar-28
Regional Cycle Centre	May-26	Jun-26	Sep-26	Mar-28
Cotham Hill	Completed	Completed	Completed	Completed
Concorde Way	Aug-26	n/a	n/a	n/a

Table 19 - BCC Milestones variance

Project Name	FBC	Contractually Committed	Construction Start	Construction Completed
Temple Way	-1 month	N/A	+1 month	0 months
Union Street	+1 month	N/A	+2 months	+2 months
Bond Street	+13 months	N/A	+14 months	+17 months
Redcliffe Roundabout	+13 months	N/A	+11 months	+15 months
Bedminster Bridges	+6 months	N/A	+10 months	+5 months
A4 Portway Corridor	-3 months	N/A	+13 months	+2 months

Portway P&R Hub	+1 month	N/A	+1 month	+4 months
WP1 - Victoria Street / Colston Ave	+1 month	N/A	+3 months	+5 months
WP2 - Southern Section	0 months	N/A	+4 months	-3 months
WP3 - Central Section	-2 months	N/A	N/A	N/A
WP4 - Active Travel	+10 months	N/A	+13 months	+4 months
WP5 - North View	0 months	N/A	N/A	N/A
A4018 (Passage Road)	N/A	N/A	+13 months	+16 months
Bristol Bridge VMS Signals	0 months	0 months	0 months	0 months
Bedminster Green	0 months	0 months	0 months	0 months
A38 South Metrobus Extension	0 months	N/A	0 months	+2 months
East Bristol Liveable Neighbourhood	+1 month	N/A	+12 months	+4 months
Streetspace 1	-1 month	N/A	+2 months	0 months
Streetspace 2	+10 months	N/A	+10 months	+15 months
South Bristol Liveable Neighbourhood	+8 months	N/A	+13 months	+24 months
Harbour Walkway	N/A	0 months	N/A	+4 months
Bristol Temple Quarter	+1 month	N/A	+3 months	+11 months
Regional Cycle Centre	+8 months	N/A	+8 months	+12 months
Cotham Hill	0 months	0 months	0 months	0 months
Concorde Way	+12 months	N/A	N/A	N/A

Table 20 - BCC scope changes

Project	Status	Amendment
Bristol City Centre business case work	N/A	Budget for business case development

Temple Way	Delivery	N/A
Union Street	Y	Remove High St/Wine St sections because S106 from St Mary le Port development unlikely to arrive in time. Remove middle section of Union St due to delay with Galleries development. Proposed 2 way working of Union St is retained however
Bond Street	Pre-FBC	N/A
Redcliffe Roundabout	Delivery	No longer upgrading southern footway on Redcliffe Way. Reduce scope of pennant stone adjacent to St Mary Redcliffe and reduce scope of public realm interventions at Freshford Lane and Portwall Lane Gardens. Reuse paving rather than replace.
Bedminster Bridges	Pre-FBC	Leave bus stops and pavement as existing on East side of Redcliffe Hill. Leave Prewitt St junction as is. Use existing paving at Regent Rd junction. Coronation Road to remain as existing except for two-way cycle route replaced by inbound-only cycle route set out with wands.
A4 Portway Corridor	Delivery	Remove kerb widening, street lighting and footway resurfacing from phase 2E. Maintain existing kerb line in phase 2D due to clash with gas main, however, this is in line with the planned benefits of a 3.5m wide pavement along the whole scheme. Move resurfacing back from maintenance fund into project budget.
Portway P&R Hub	Delivery	N/A substantially completed
Stockwood Preparatory Business Case	N/A	Budget for business case development
WP1 - Victoria Street / Colston Ave	Delivery	N/A
WP2 - Southern Section	Delivery	N/A
WP3 - Central Section	Y	Remove project from scope, the with exception of the College Green/Anchor Road early funding works.
WP4 - Active Travel	Pre FBC	N/A
WP5 - North View	Pre FBC	N/A
A4018 (Passage Road)	Delivery	N/A
Bristol Bridge	Completed	N/A

Bedminster Green	Pre FBC	N/A
A38 South Metrobus Extension	Delivery	N/A
East Bristol Liveable Neighbourhood	Pre FBC	N/A – independent review in progress
Streetspace 1	Completed	N/A
Streetspace 2	Pre-FBC	N/A
South Bristol Liveable Neighbourhood	Pre FBC	N/A
Harbour Walkway	Delivery	N/A
Bristol Temple Quarter	FBC*	FBC conditionally approved, no scope changes
Regional Cycle Centre	Pre FBC	N/A
Cotham Hill	Completed	
Concorde Way	Pre FBC	N/A
Bristol unallocated general		

OFFICER DECISIONS

Key Considerations

97. The table below outlines the delegated decisions taken by the Executive Director of Transport in consultation with the equivalent Unitary Authority Directors, for projects between January and March 2026.

Date of Decision	Project	Decision Taken
08/01/2026	Bath City Centre Phase 1	1) Approved the Full Business Case for Bath City Centre Phase 1 and the award of £3,330,749 of CRSTS capital funding to Bath & North East Somerset Council, beyond the £701,000 early works funding already awarded for the delivery of the scheme.
08/01/2026	Micromobility Physical Parking Infrastructure	1) Approved the Feasibility and Development Application Form to release £70,000 of CRSTS funding to support Micromobility Physical Parking Infrastructure.
08/01/2026	West of England Regional Transport Model	1) Approved £750,000 of CRSTS capability funding for the delivery of the West of England Regional Transport Model (WERTM) rebase.
16/01/2026	Muller Road Phase 2	1) Approved the updated spend profile for Muller Road Phase 2 project. 2) Approved the delay of FBC submission from July 2025 to June 2026. 3) To note the widened scope to include speed calming on Ralph Road and footway widening near Fairfield High School to deliver additional community benefits.
16/01/2026	Concorde Way (Dovercourt Road)	1) Approved the updated spend profile of the Concorde Way (Dovercourt Road) project. 2) To note that the project is now producing a Low Risk Transport Scheme (LRTS) Business Case rather than an Outline Business Case.
13/02/2026	New Cut Bridges (Maintenance Challenge Fund)	1) Approved the revised spend profile for the New Cut Bridges programme.
13/02/2026	Bath to Bristol Strategic Corridor	1) Approved that the project scope and schedule are as per the details provided in the recently finalised CRSTS re-baselining submission for the DfT. 2) Approved the additional drawdown from the existing project budget of £3,814,607 to account for the current estimated cost to bring the schemes to FBC stage

26/02/2026	CRSTS Re-baseline - West of England Mayoral Combined Authority	1) Approved the West of England Mayoral Combined Authority CRSTS Programme re-baseline delivery plan and the submission of a programme level change request to the Department for Transport. The re-baselined headline figures are shown in the tables below. The overall allocation increased from £147.93m to £168.23m.
26/02/2026	CRSTS Re-baseline - South Gloucestershire Council	1) Approved the South Gloucestershire Council CRSTS Programme re-baseline delivery plan and the submission of a programme level change request to the Department for Transport. The re-baselined headline figures are shown in the tables below. The overall allocation increased from £162.36m to £163.52m.
26/02/2025	CRSTS Re-baseline - Bath and North-East Somerset Council	1) Approved the Bath and North-East Somerset Council CRSTS Programme re-baseline delivery plan and the submission of a programme level change request to the Department for Transport. The re-baselined figures are shown in the tables below. The overall allocation increased from £62.55m to £69.99m. 2) Note the early warnings for the projects listed in this document, which will require further changes to scope, time, funding profiles and potentially funding allocations. 3) Endorse the plan for further checkpoints for these projects with early warnings.
26/02/2026	CRSTS Re-baseline - Bristol City Council	1) Approved the Bristol City Council CRSTS Programme re-baseline delivery plan and the submission of a programme level change request to the Department for Transport. The re-baselined headline figures are shown in the tables below. The overall allocation increased from £161.89m to £179.31m
05/03/2026	Bristol City Centre Union Street	1) Approved the Early Works Funding application and award of funding to Bristol City Council of £4,200,000 for Bristol City Centre Union Street for delivery of utilities works, preparatory works, taxi ranks and disabled bays.
05/03/2026	CRSTS Re-baseline - West of England Mayoral Combined Authority	1) Approved the West of England Mayoral Combined Authority CRSTS Programme re-baseline delivery plan reprofiling changes associated with the revised delivery plan and allocations. 2) Approved the change of award for the project noted below.
05/03/2026	CRSTS Re-baseline – Bristol City Council	1) Approved the Bristol City Council CRSTS Programme funding awards associated with the re-baseline delivery plan 2) Approved the changes to funding and profiles for the projects noted below.

12/03/2026	CRSTS Re-baseline – South Gloucestershire Council	1) Approved the South Gloucestershire Council CRSTS Programme re-baseline delivery plan reprofiling changes associated with the revised delivery plan and allocations. 2) Approve the awards of additional funding for the projects.
12/03/2026	CRSTS Re-baseline – Bath and North East Somerset Council	1) Approved the Bath and North-East Somerset Council CRSTS Programme re-baseline delivery plan reprofiling changes associated with the revised delivery plan and allocations. 2) Approve the awards of additional funding for the projects.
